

TRANSFORM LEARNING SPACES 2013

HASSELL



PROJECT OUTCOMES

To establish a refurbishment program for Learning and Teaching Spaces (CATS and SATS) more often and for longer to reflect contemporary pedagogies and learning technologies.

To complete the refurbishment of all identified spaces for a Semester 1 2014 commencement.

To provide engaging CATS spaces which support the Transforming Learning @ Curtin initiative.

To improve professional development opportunities for CU academic staff through the use of a model collaborative teaching/CU training space.

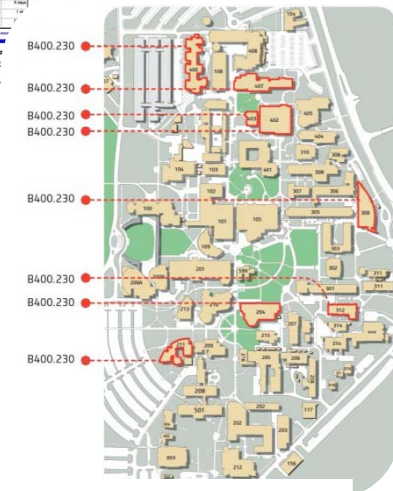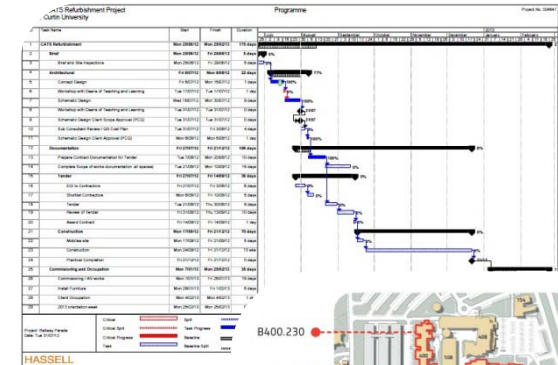

2012 PROGRAM

Classroom Refurbishment Program: Stage 1



Classroom Refurbishment Program: Stage 1



2012 PROGRAM

Classroom Refurbishment Program: Stage 1



Classroom Refurbishment Program: Stage 1



2012 PROGRAM

Classroom Refurbishment Program: Stage 1



Key Learnings from Stage 1

NETWORK/ INFRASTRUCTURE

Network and infrastructure limitations influences priorities

EXAMINATIONS TIMETABLING

Use of rooms for examinations influences requirements for power and room layouts.
Room availability and examination locations influence construction programs.

REMOTE COLLABORATION

Use of rooms for remote collaboration influences requirements for

- vision/sound/layouts
- Audio visual equipment and integration


PROCUREMENT

Due to the time constraints contractors will be appointed on a rates basis to enable work to commence in November 2013. AV Integration still problematic.


FUTURE PROGRAMS

Included in the 2013, 2014, 2015 Physical Facilities Plans are provisions for ongoing T&L Refurbishments. Feedback from the 2012 program being gathered and used.

Elsewhere - RMIT

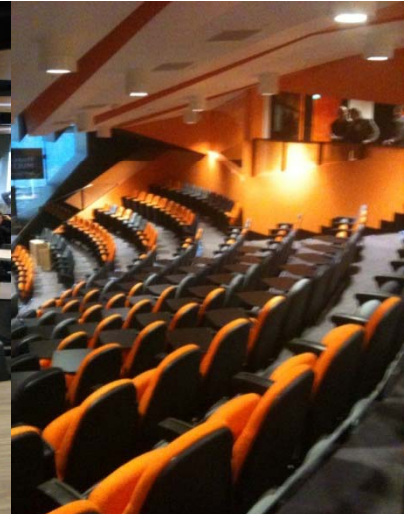


Elsewhere - QUT

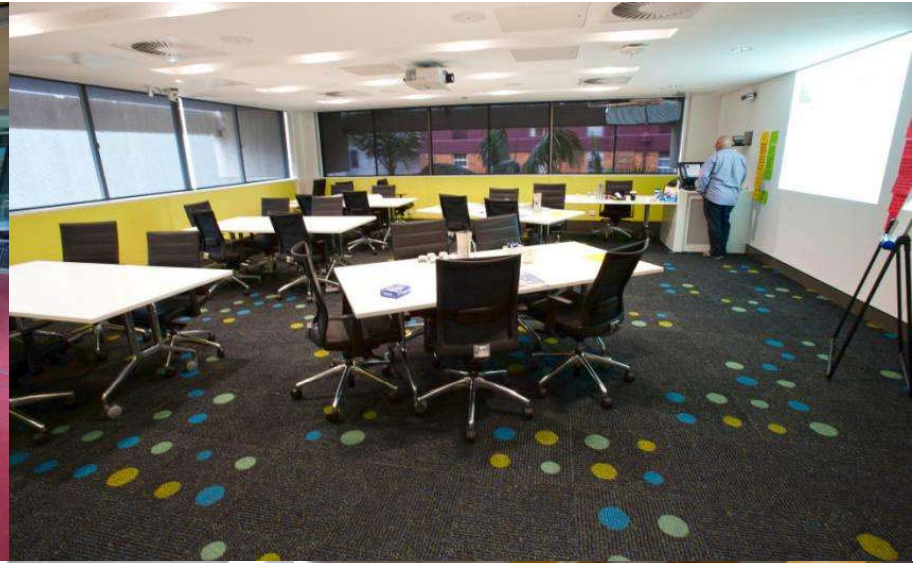


Elsewhere - UWA



New Generation Learning Spaces – 2013




2013 PROGRAM – selected spaces

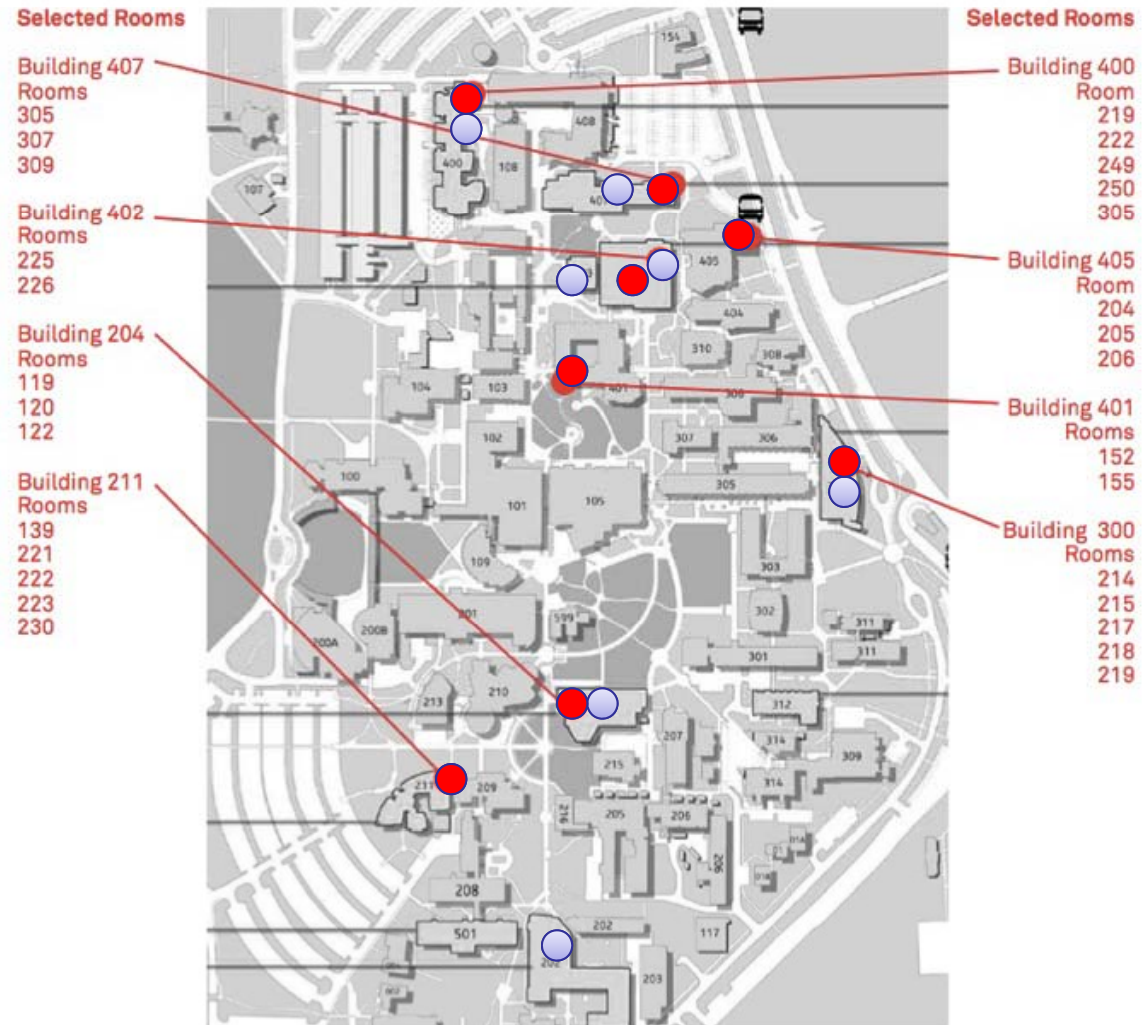



2013 PROGRAM- Approach

Flexible

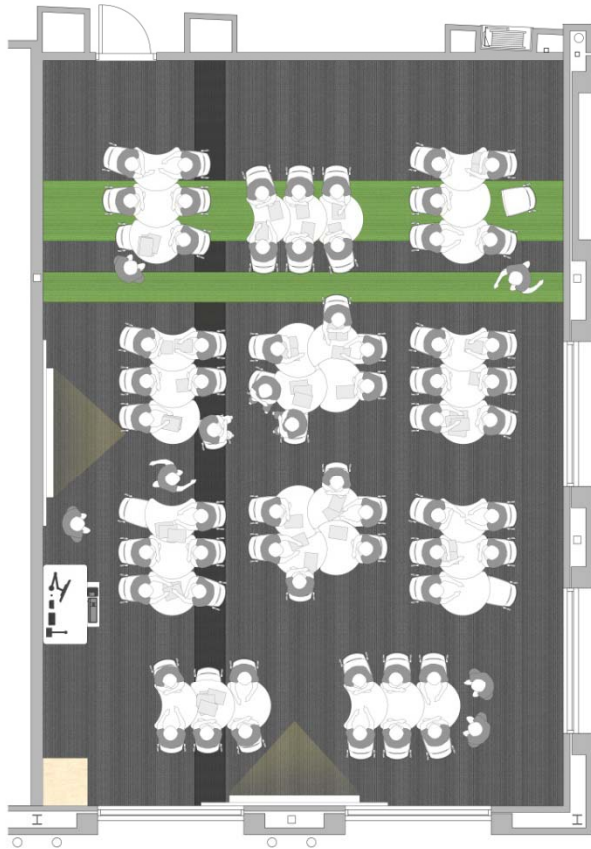


2013 PROGRAM- Approach

Semi Flexible

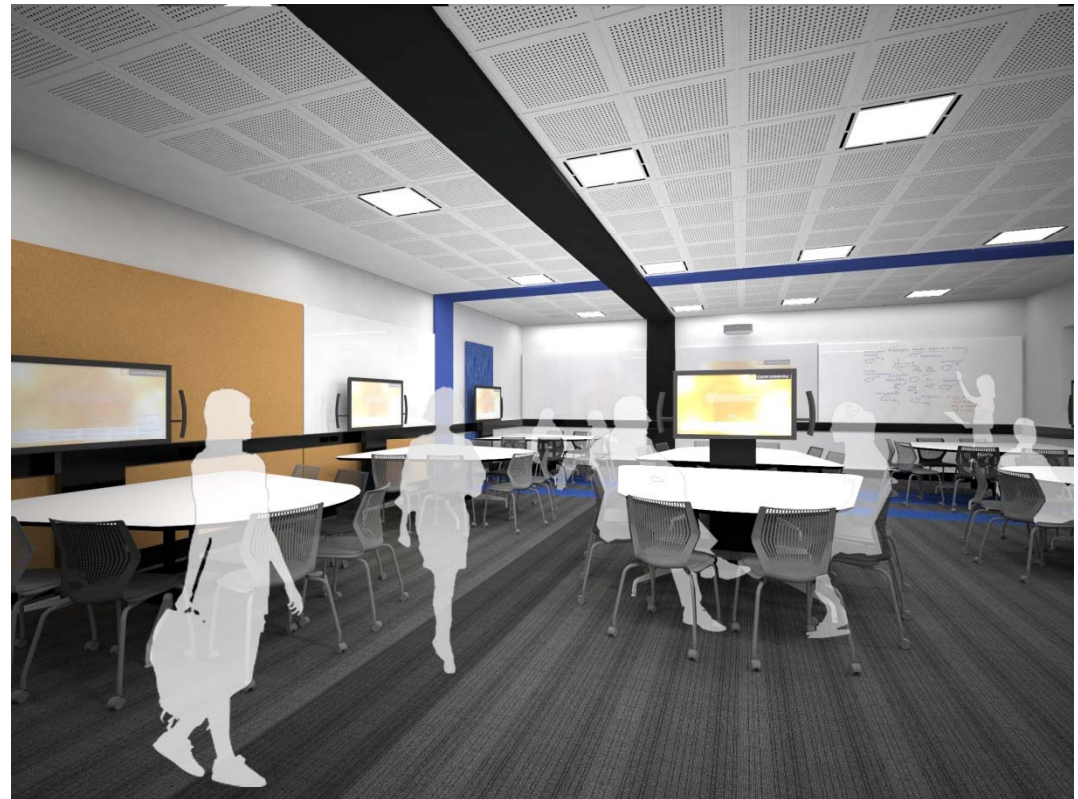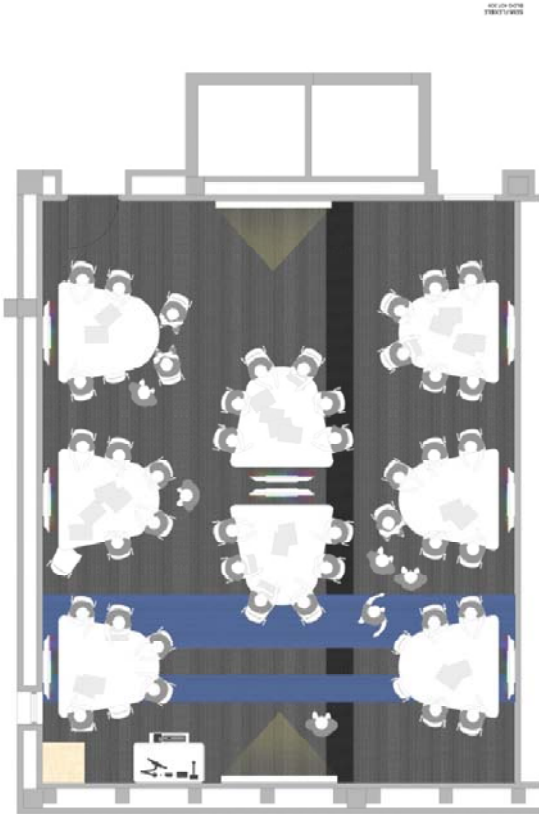

2013 PROGRAM- Approach

Fixed

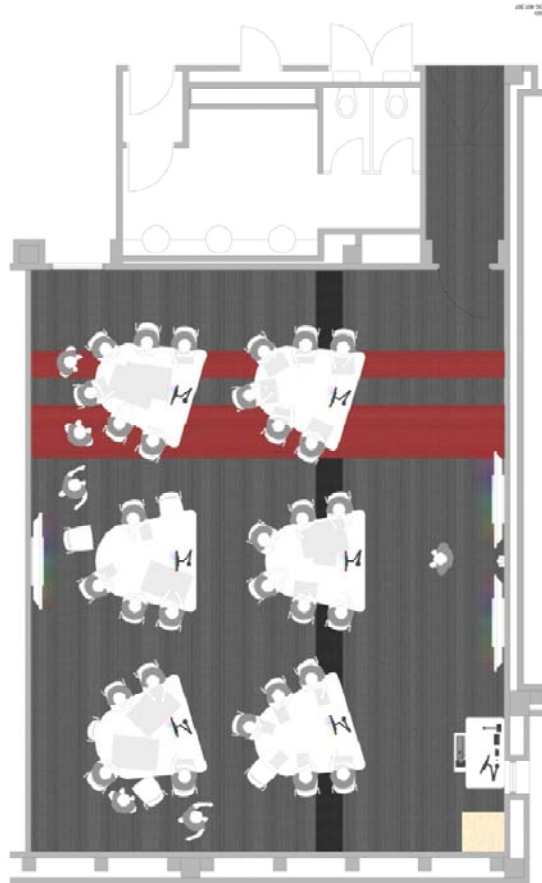

2013 PROGRAM- Approach

Distributed – Remote Collaboration



2013 PROGRAM- Update on Progress



Progress

- Contractors have been engaged for the refurbishment works
- Demolition works commenced
- AV functionality has been finalised
- Furniture has been ordered

On Track

- Stage completion due late January / early February 2014
- Ready for occupation Semester 1 2014

Transforming Learning @ Curtin

<http://www.youtube.com/watch?v=5hBFJq59BAg>



TRANSFORM LEARNING SPACES 2013

HASSELL
